

Where are we? - High Level Programme for Bray and Taplow Towers (subject to change)

Mar-22 Apr-22 May-22 Jun-22 Jul-22 Aug-22 Sep-22 Oct-22 Nov-22 Dec-22 Jan-23 Feb-23 Mar-23 Apr-23 May-23 Jun-23 Jul-23 Aug-23 Sep-23 Oct-23 Nov-23 Dec-23 Jan-24 Feb-24 Mar-24 Apr-24 May-24 Jun-24 Jul-24 Aug-24 Sep-24 Oct-24 Nov-24

Site set up



Build scaffolding



Carry out roof works



Replace windows independently across the building (including soft start for quality)



Install new windows at pace



96% - About 300 homes


Install cladding rails, cement boards, insulation and external fire stopping



Replace the roof and install BMU



Remove scaffolding from top down floor by floor as windows are replaced and cladding gets installed



Replace the windows to ground and 1st floors




Replace brick work



Remove scaffolding below ground and install insulation



Where are we? - High Level Programme for Dorney & Burnham Towers (subject to change)

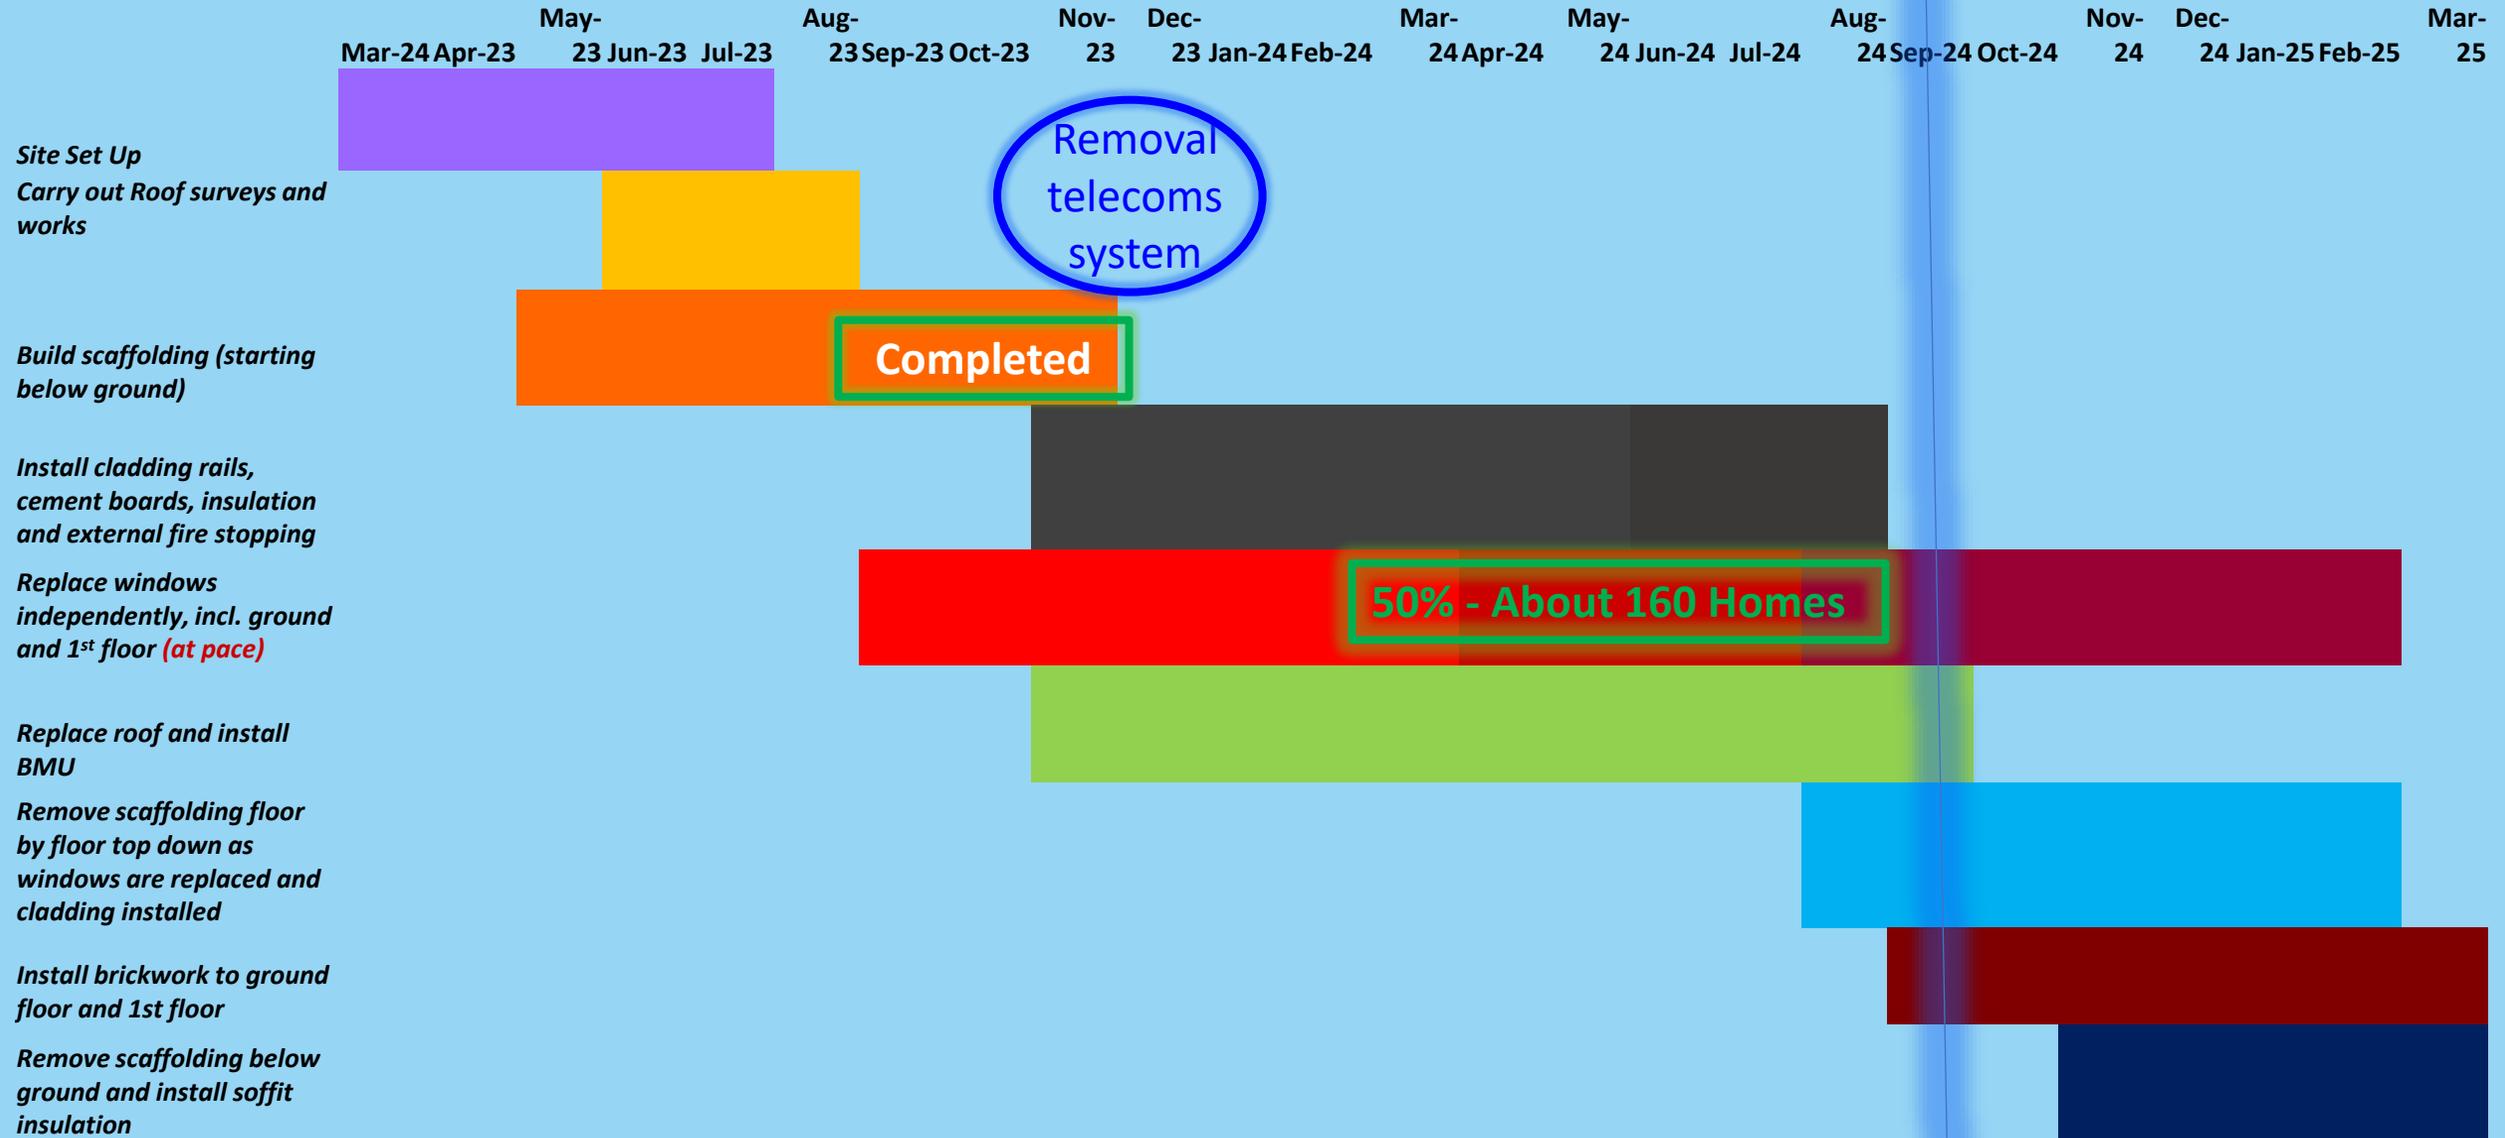


Bray and Taplow Towers - Facade Installation **PROGRESS** as at 25 September



Bray					
Floor					
22	Completed	Completed	Completed	Completed	Completed
21	Completed	Completed	Completed	Completed	Completed
20	Completed	Completed	Completed	Completed	Completed
19	Completed	Completed	Completed	Completed	Completed
18	Completed	Completed	Completed	Completed	Completed
17	Completed	Completed	Completed	Completed	Completed
16	Completed	Completed	Completed	Completed	Completed
15	Completed	Completed	Completed	Completed	Completed
14	Completed	Completed	Completed	Completed	Completed
13	Completed	Completed	Completed	Completed	Completed
12	Completed	Completed	Completed	Completed	Completed
11	Completed	Completed	Completed	Completed	Completed
10	Completed	Completed	Completed	Completed	Completed
9	Completed	Completed	Completed	Completed	Completed
8	Completed	Completed	Completed	Completed	Completed
7	Completed	Completed	Completed	Completed	Completed
6	Completed	Completed	Completed	Completed	Completed
5	Completed	Completed	Completed	Completed	Completed
4	Completed	Completed	Completed	Completed	Completed
3	Completed	Completed	Completed	Completed	Completed
2	Completed	Completed	Completed	Completed	Cladding Installed
1	Completed	Completed	Completed	Completed	Cladding Installed
G	Completed	Completed	Completed	Completed	Cladding Installed

Taplow					
Floor					
22	Completed	Completed	Completed	Completed	Completed
21	Completed	Completed	Completed	Completed	Completed
20	Completed	Completed	Completed	Completed	Completed
19	Completed	Completed	Completed	Completed	Completed
18	Completed	Completed	Completed	Completed	Completed
17	Completed	Completed	Completed	Completed	Completed
16	Completed	Completed	Completed	Completed	Completed
15	Completed	Completed	Completed	Completed	In progress
14	Completed	Completed	Completed	Completed	In progress
13	Completed	Completed	Completed	Completed	Completed
12	Completed	Completed	Completed	Completed	Completed
11	Completed	Completed	Completed	Completed	Planned
10	Completed	Completed	Completed	Completed	Planned
9	Completed	Completed	Completed	Completed	Completed
8	Completed	Completed	Completed	Completed	Planned
7	Completed	Completed	Completed	Planned	Planned
6	Completed	Completed	Completed	Completed	Completed
5	Completed	Completed	Completed	Completed	Planned
4	Completed	Completed	Completed	Completed	Planned
3	Completed	Completed	Completed	Completed	Completed
2	Completed	Completed	Completed	Completed	Planned
1	Completed	Completed	Completed	Completed	Cladding Installed
G	Completed	Completed	Completed	Completed	Completed

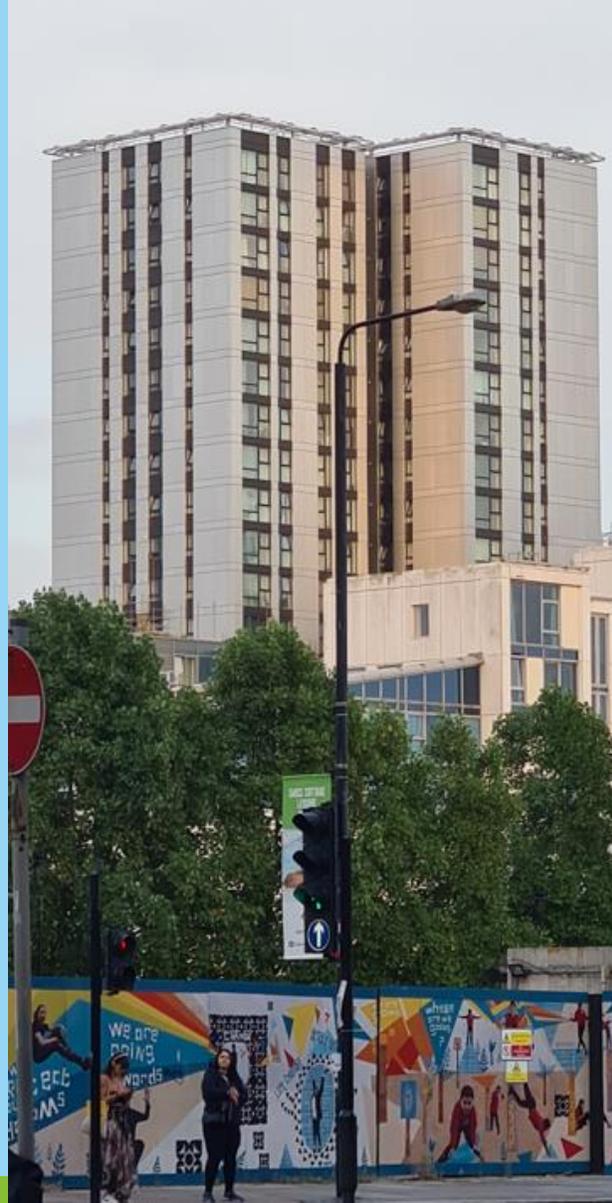

 Completed	 Cladding Installed
 In progress	
 Planned	
 Subject to scaffold removal and access	

Subject to Access into Homes

